


BS5837 2012 Tree Information – Tredegar Park Lodge

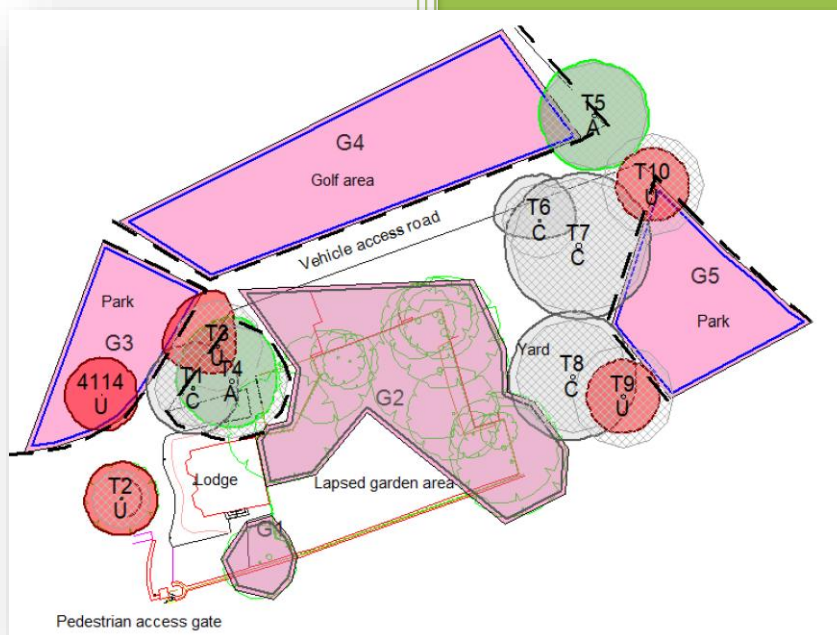

Site Address:

Tredegar Park Lodge
Tredegar Park
Duffryn
Newport
NP20 3AQ

James Pinder Tech Cert (Arbor A)

james@treecareconsulting.co.uk

07939 150 457


01633 882 890

Contents

Contents.....	2
Site Location/descriptions	4
Report Limitations.....	5
Definitions.....	6
Avoiding damage to trees during construction	7
How to protect trees from preventable damage.....	9
Tree Protection Fences	9
Soils	10
Stripping/delivering soil	10
New soils to site	10
Ground Protection (if required).....	11
Methods and specifications of paths using cellular confinement systems	12
Risk factors include	12
Compaction.....	12
Digging surfaces (site strip).....	12
No dig.....	12
Cellular Confinement and Backfill Material.	13
Surfacing Options.....	14
Block Paving:	14
Tarmac:	14
Loose Gravel:.....	14
Grass Blocks:	14
Site do and Don'ts	15
RPA dos & don'ts.....	15
Arboricultural Watching Brief (AWB).....	16
Tree Data.....	17
Minimum Arboricultural Method Statement –.....	19
Site Monitoring by AWB.....	20
Arboricultural Implications Assessment – AIA (surveyor's overall thoughts).....	21
Tree Work List	22
Felling list	22
Pruning works	22

Coppicing works.....	22
Transplanting works.....	22
Planting list.....	22
Data Sheets - site survey carried out - 26/07/2023.....	23
Individual Trees Schedule:	23
Groups of Trees Schedule:	25
Site Plans – Key	26
Site Plan (Screen grab – please see scale pdf plan)	27

Site Location/descriptions

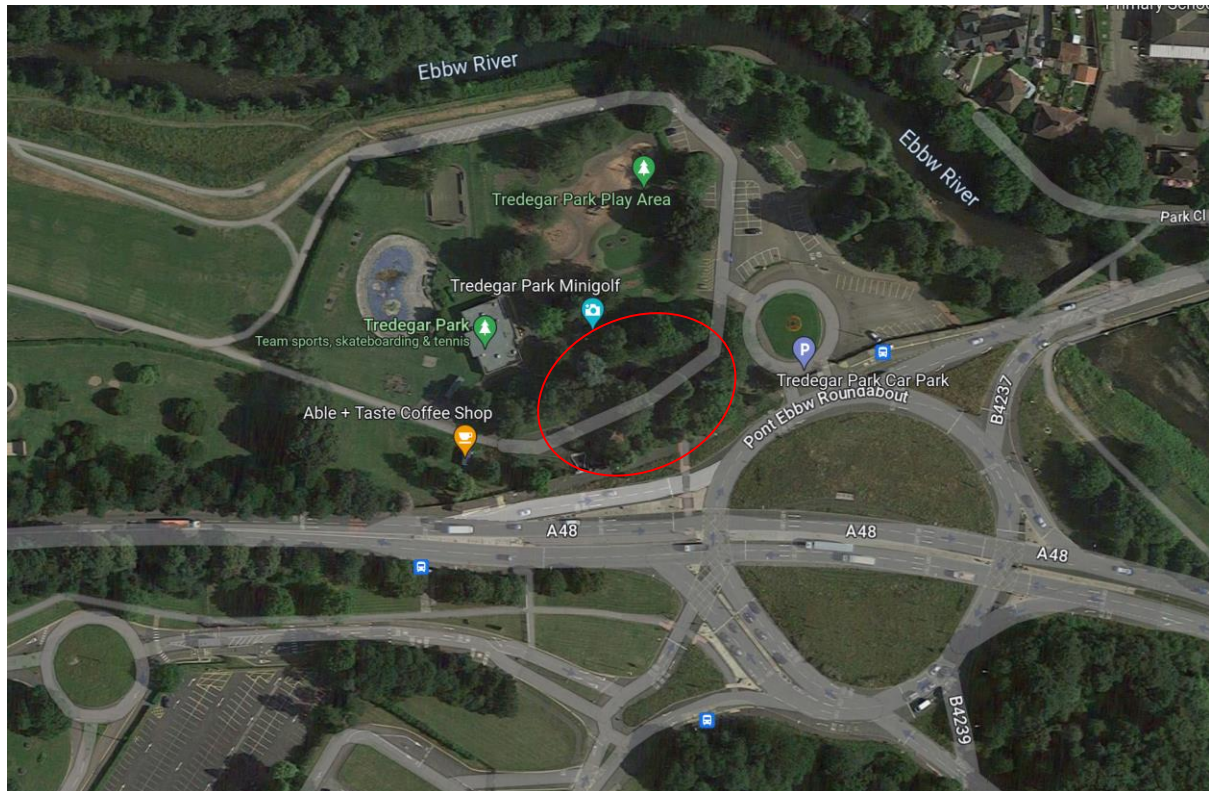

- I accessed the site from the Pont Ebbw Roundabout.
- The site is owned by my client.
- There are trees on site which could be affected by development activity.
- Some management recommendations have been made regarding trees due to age, form and long-term management/landscape.
- The grounds are laid out as formal park landscape with a wide range of tree species and ages.
- Further planting should take place as a final landscaping scheme to replace lost trees to due defects the project has now highlighted.

Report Limitations

- Visual inspections from ground level unless otherwise indicated.
- No invasive inspection techniques used unless indicated.
- No underground excavations will have been performed unless otherwise indicated.
- No climbing or inspection at height will have been involved unless indicated.
- Report information expires after twelve calendar months from report issue date.
- Reports and information relating to them are the property of Treecare until paid for in full. Information within reports is retained at Treecare's discretion until paid for in full. Treecare will retract reports and comments from any due process if not paid for in full.
- Treecare will not create access to trees unless directed yet will undertake the accessing work if contracted to do so.
- Where access to a tree is not possible, best judgement/estimation will be used. Accurate information will therefore be minimal and will be checked at the earliest opportunity.
- Treecare only use suitably trained and knowledgeable persons for inspections holding the relevant qualifications for their purpose.
- Treecare has the right to remove employees from danger as they see fit.
- Verbal comments on buildings structural integrity are an opinion not fact (a structural engineer will be required for a detailed analysis).
- The diagrams and drawings provided by Treecare are not exact and should not be used for design purposes unless directed otherwise. They are however indicative of site features.
- Treecare will try their very best for the client. However, conflict of interest or professional judgement and character clashes must be accepted and resolved.
- Treecare's information and advice will only last as long as current legislation and current knowledge is up to date. Should new information supersede previous comments a new report must be issued.
- This is a preliminary report and further more detailed aspects may be required by the LPA or client at a later stage to define exact processes.

Definitions

BS 5837 2012 (Trees in relation to construction) was revised in 2012 and now supersedes the previous 1991 & 2005 editions.

Within the newer BS many definitions are given so the professional arboriculturists are able to give an indication to planners and architects so that a common understanding of trees and how building new structures may affect the health and support of trees can be given.

Arboriculturist

A person who through relevant training, qualifications and experience in the arboricultural world is able to form an opinion on how trees may be affected through development processes.

Competent person

A person, who has had training and experience relevant to the matter in hand and is able to recognize whether it is safe to proceed with a specific site process.

Structure

Man-made object, such as a building, carriageway, path, wall, services and built or excavated earthworks.

Root protection area (RPA)

A site layout design tool that enables a pictorial representation of trees required rooting area. This area must be protected to ensure the survival of trees.

Tree constraints plan (TCP)

A clear plan diagram showing tree locations, crown spreads and rooting areas. This allows the arboriculturist to demonstrate areas where trees will affect a proposal by tree volume, height or shade.

Construction exclusion zone (CEZ)

An area clearly marked both on site and on a site plan. This area must have no construction operations carried out within.

Tree protection plan (TPP)

A scale drawing that shows tree locations, rooting areas and fencing locations on site.

Arboricultural implications assessment (AIA)

An assessment made by the arborist to identify, evaluate and possibly mitigate effects of construction process on trees.

Arboricultural method statement (AMS)

A written or toolbox talk applied method of ensuring the contractor (construction) can implement the design adjacent to existing trees.

Services

Above or below ground pipe work, wire or ducting construction that could affect trees crowns or their roots or rooting areas.


Special engineering

Designing of a structure with the physiological requirements of trees as the primary concern.

Avoiding damage to trees during construction

The flow diagram below shows the process that should be followed to help prevent any risk of damaging trees during the design and construction process and due consideration to retained trees and roots is given. Where any confusion lies or something noted is not understood it is important that the query is resolved before proceeding.

The arboriculturist should be consulted and, as a minimum a verbal discussion must take place in order to clarify any detail that is misunderstood.

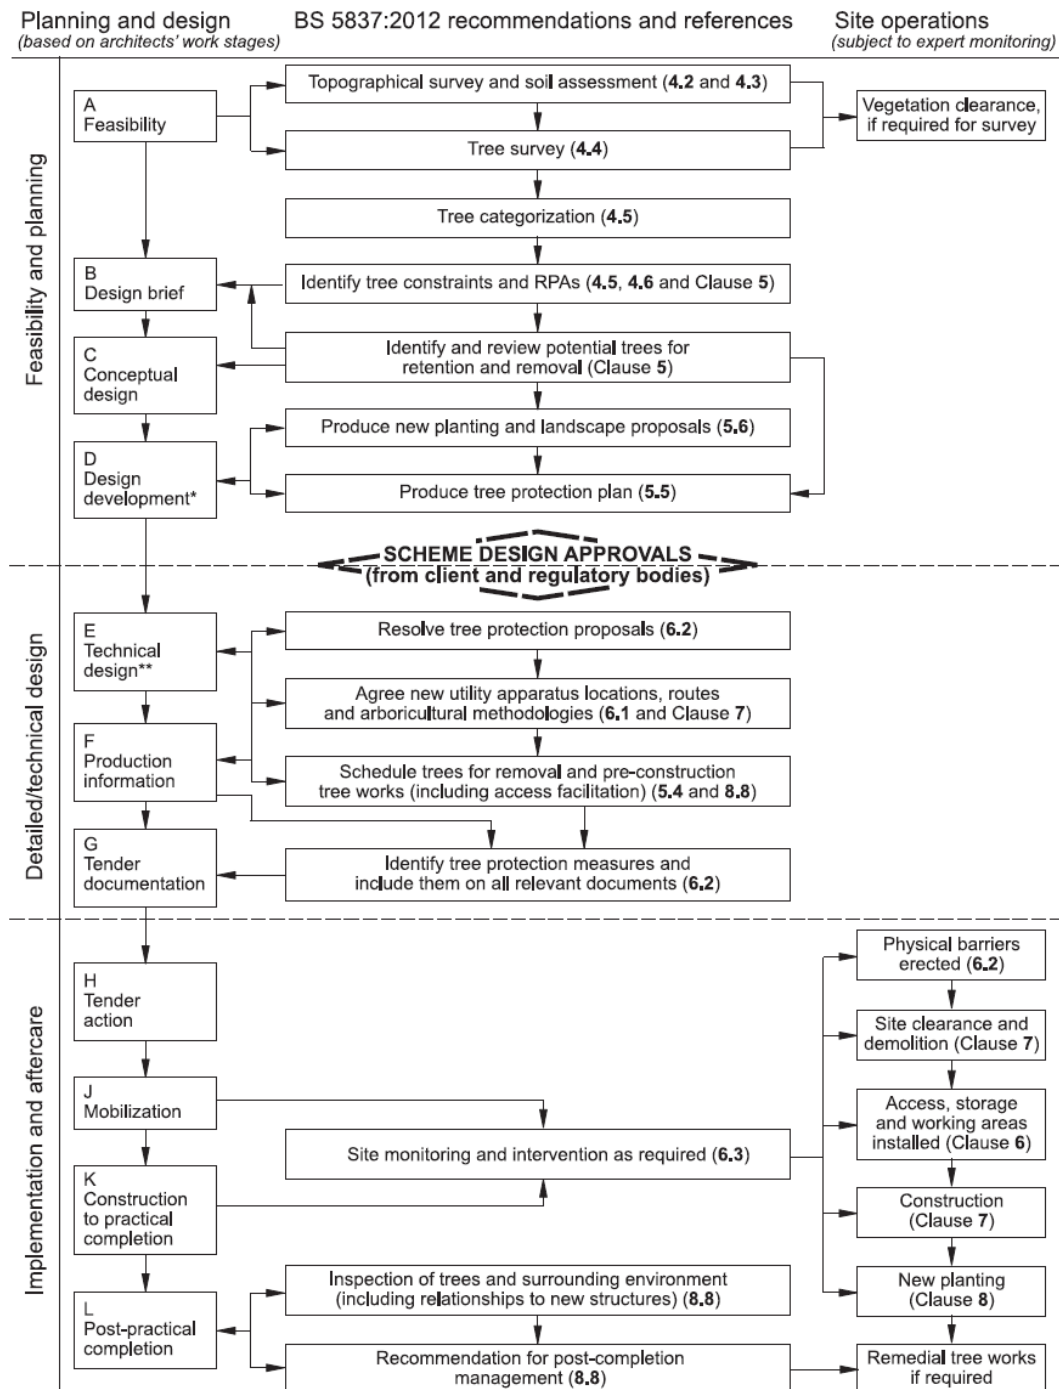

Trees on development sites are commonly destroyed by plant equipment operators feeling that their own experience of trees outweighs the knowledge and experience of the arboriculturist. In my opinion this would be a very rare occurrence.

Damage occurs by many differing ways. There is indirect and direct damage. The first takes time to have an effect on long term tree health unless toxic substances are involved, the latter can be instant but can lead to a drop in tree value or create a wound a tree finds difficult to defend.

Compaction of soils can cause many problems for trees and must be avoided at all costs. The compaction of a soil will remove the pore spaces between soil particles and thus remove oxygen from the soil that the tree would use for respiration. This then means that the tree will slowly but surely decline as it is suffocated.



This photo shows a combination of damage. The roots have been severed or damaged in such a way that stability has been lost and this tree was felled. If the same damage had not led to an immediate tree failure the tree would have been sent into an irreversible spiral of decline.

The loss of roots will have caused a lack of structural support, loss of moisture take-up, loss of oxygen take-up and a means of the tree storing energy as starch within root structures. This type of root damage causes a slow decline in tree foliage known as crown die back.

The picture to the right shows the die back of foliage several years after the completion of a development site. Machine operators will often mention how they have dug roots or driven over them. This is what happens once they leave site.



Trees have to have roots in order to perform their most basic but important tasks. To the tree the root system is more important than the crown. However, the crown is more important to us as it is the part we can see.

The only way to avoid needless destruction is to give them the space they require and provide adequate protection from construction process.


If adequate protection is not given the disaster below is not far behind!



How to protect trees from preventable damage

Tree Protection Fences

The BS document provides various diagrams on how to protect tree rooting areas. The fence needs to be erected prior to construction traffic site occupation and often with the arboriculturist present to ensure correct placing. Types for hard and soft ground surfaces are shown below.

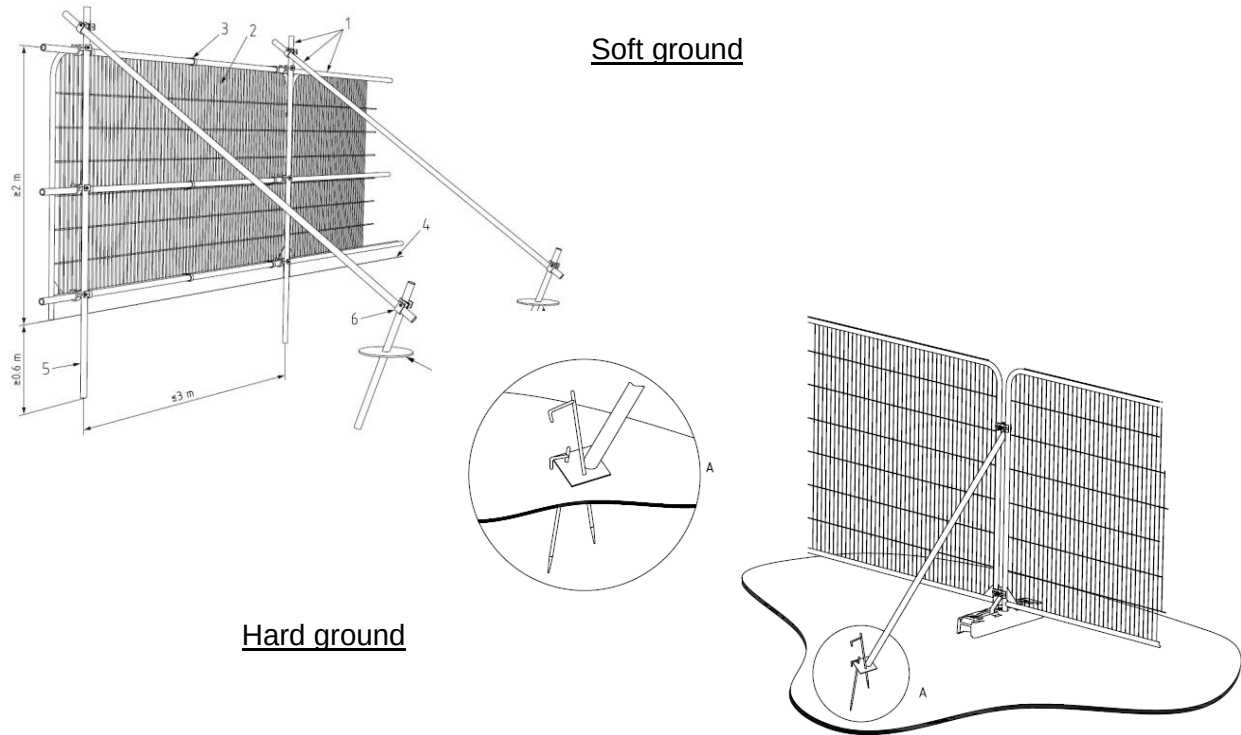

The rooting area is calculated by using a stem measurement. For single stems trees the diameter if the stem is measured at 1.5m above ground level or point of even stem taper. This figure, in millimeters is then multiplied by twelve and this will then give the radial measurement from the stem to the edge of the rooting area. A circular area is created around the tree at the radial measurement. This is where the fencing should be located. Multi stemmed trees now require average stem size calculations based on 2-5 stems or 5+ stems. Contact the arboriculturist if in any doubt.

The design of RPA or CEZ fencing should be so that it cannot be moved during works. It must also be robust enough to withstand minor knocks and scrapes from plant equipment. The fence must be in place prior to site occupation by plant equipment and should be removed once the site has been vacated by construction traffic. Should there be a requirement to place pedestrian walkways across and RPA a suitable method of ground protection should be used. A geo textile layer, compressible material and then boards should suffice as a walkway. This specification will need to be agreed by the arboriculturist prior to installation. It should also be laid in front of the direction of travel during installation. All hedges and trees over 150mm diameter at 1.5m need root protection. If no RPA measurement is provided for a tree or hedge requiring root protection ensure the fence is set 2m from the outer edge of the tree/hedge drip line.

Fences will require clear signage as to purpose – Tree Protection Fencing.

Soils

Chapter 6 of BS 3998 2010 (British Standard for Treework) explains that adverse and sudden changes to soil structure, nutrient, oxygen and hydrology can have catastrophic outcomes for trees. Steps must be taken to protect the soils within a rooting area where retained tree roots are present. It is crucial to tree survival that soils are not altered.

A basic tactile assessment of soils by hand has been made of the site soil structures. Common soils are found to be present on site but soil condition can always be improved upon. Soil improving ameliorants can be found in Annex B, Table B2 of BS 3998 2010 where recommendations are made to improve soils on site.

BS3998 2010 advises the use of soil mulches such as woodchip and leaf mould for improving soils around trees. It is advisable that where suitable, woody material being removed from site is turned into a woodchip mulch and applied to rooting areas. This mulch improves worm activity thus increasing oxygen levels plus it adds vital nutrients to the soil environment. Mulches also help retain soil moisture levels and as such help promote growth and development in retained trees.

Stripping/delivering soil

Stripped or delivered soil to site must be stored as follows:

- Loose tipped.
- Away from contaminants.
- Clearly marked to future use.
- Foreign bodies removed.

New soils to site

- Planting pits will be new construction of the appropriate soil volume as requested by the LPA.
- Soils must be handled according to good practice as laid out in BS3882:2007 and the DEFRA code (2009).
- Imported soils will be used for the planting pit. (The ideal planting soil contains approximately 45% mineral solids, 5% organic mineral solids and 25% each water and air, as shown in Figure B.1.BS8545).
- Planting pits to only contain imported top quality planting soil/top soil mix at upper 400mm depth only, in accordance with the specifications laid out in BS3882:2007.
- Soils below 400mm must be suitable sub soil as specified by BS3882:2007 and BS8545.
- All soils used in the planting pit soil must have a certificate of compliance from the soil supplier that also states the volumes supplied.

Ground Protection (if required)

Existing soil structure and texture must not be destroyed or altered in the vicinity of trees and rooting areas. Future planting sites should also have their structure preserved by the use of ground protecting plates. This will allow mechanical plant to move around the site and transit areas of high root occupancy or planting sites of high value without damaging important soils.



The use of ground protecting boards such as these seen in the adjacent picture should be used. Geo textile and felt may be required beneath these routes to minimize puddling of the soil surface. Should puddling occur, a capped layer may well be formed which will reduce the lateral diffusion of soil gasses and cause significant problems for retained trees.

A non-compressible layer such as woodchip should be used under-ground protection whenever there is a need for it to be in place for more than three days.

Any ground protection must be capable of withstanding the load placed upon it. An engineer must be consulted for advice on the specification of such protection if required for the area if high loads are to be expected.

Another method of ground protection for light operations such as pedestrian activity can be utilized by using the installation of raised platforms mounted onto scaffold legs.

Platforms such as these could be used for light storage, walkways or as an area for construction workers to stand whilst carrying out operations such as block laying and pointing. Water proof sheeting on top of the boarding should be used to catch any material that could leach into soils where tree roots are present or run off could reach.

Particular attention should always be made when using ground protection to surface run off. Fuel oils, cement and water with high fines content are all very damaging to trees. Provision must be made to ensure that run off does not leach into soils.

Temporary track ways can also be constructed by using geo textile onto top of the ground and type 1 road stone with no fines be used as the surface. This method must only be used at the outer limits of an RPA.

Methods and specifications of paths using cellular confinement systems

When considering possible damage to tree roots during the applications of vehicular access and parking, the risk to trees is from oxygen depletion caused by compaction of subsoils and site clearance work damaging the soil structure and roots below ground.

This damage may well lead to tree failure and can be traced back to the contractor responsible for liability claims.



Risk factors include

Creating an impermeable surface
Causing a rise in the water table due to construction
Increasing ground level
Contamination of subsoil's

Compaction

When looking at site conditions and use, the following information should be considered to enable a load bearing structure capable of supporting traffic to be proposed:

Californian Bearing ratio (CBR) – Standard test method for measuring soil strength
Soil types
Water table
Maximum load (vehicles)
Acceptable rut depth

Reinforcement type - Cellular Confinement
Type and Depth of engineered infill material - Clean, angular. Usually, 40mm to 20mm.

Digging surfaces (site strip)

Site stripping does damage root structures present prior to construction; however, the use of no-dig construction elevates the access road requiring edge protection.

No dig

1. Remove surface vegetation
Use a suitable herbicide suitable for the specific vegetation and not harmful to the tree root system.
2. Place geo textile separation filtration layer
Use a Fibretex F4M non-woven Geo textile over the prepared sub-grade. Overlap dry joints by 300mm.
3. Cellular Confinement System
The three-dimensional cell structure, is formed by ultrasonically welding polyethylene (perforated) strips / panels together to create a three-dimensional network of interconnecting

cells. A high degree of frictional interaction is developed between infill and the cell wall, increasing the stiffness of the system.

4. Edge restraint

A treated timber edging is usually acceptable.

Cellular Confinement and Backfill Material.

Expand the confinement systems 2.56m wide panels to the full 8.1m length. Pin the panels with staking pins to anchor open the cells and staple adjacent panels together to create a continuous mattress. Infill the cells with a no fines angular granular fill (typically 40-20mm) within each open cell. The use of cellular confinement reduces the bearing pressure on the subsoil by stabilizing aggregate surfaces against rutting under wheel loads. Comparisons between cellular confinement and traditional aggregate and geo grid-reinforced structures demonstrate a 50% reduction in construction thickness of the granular material.



Surfacing Options

Block Paving:

1. Lay second layer of Fibretex F4M Geo textile separation fabric over the filled confinement sections.
2. Lay sharp sand bedding layer compacted with a compaction plate to recommended depth to consolidate but not compact.
3. Lay block pavers as per manufacturer's instructions.

Tarmac:

Place 25mm layer of the granular material above the confinement system and lay the bitumen base and wearing courses.

Loose Gravel:



1. Place second layer of Fibretex F4M Geo textile separation fabric over the filled confinement sections.
2. Place decorative aggregate to required depth.

NOTE: A treated timber edge should be provided to restrict gravel movement.

Grass Blocks:

1. Place second layer of Fibretex F4M Geo textile separation fabric over the filled confinement sections.
2. Place 50/50 root zone bedding layer to the required depth.
3. Lay recycled Duo Block 500 Grass Protection System filled with 50/50 root zone mix.
4. Seed as per architect's instructions.
5. (Alternatively, the Grass Blocks may be filled with gravel.)

Below are illustrations of the correct stapling procedure for joining both edges and ends of panels together;

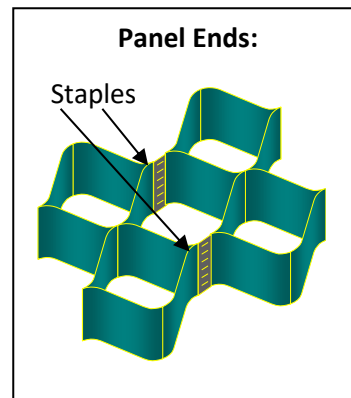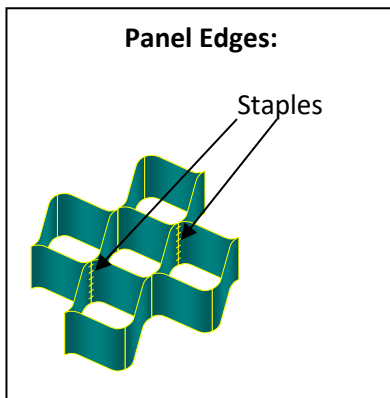

Site do and Don'ts

- Do not occupy ground space within the crown spread of a tree.
 - Do not work without suitable protection fencing around retained trees.
 - Do not travel the site without suitable ground protection where roots exist.
 - Do not break the ground near trees unless being supervised by a competent person in tree care and management.
 - Do not allow builders sand to be placed near rooting areas as this is toxic to trees.
 - Do not store fuels, cement or other toxic materials near trees.
 - Do not light fires within 15m of a tree crown.
 - Do not trench through roots above 10mm in diameter unless under direct supervision by an arboriculturist.
 - Do not lean objects against tree stems or branches.
 - Do not tie ropes or cables to trees unless during a temporary and authorized task.
 - Do not allow plant equipment to make contact with any part of trees.
 - Do not allow exhaust pipes to be directed at trees and shrubs.
 - Do not place service or drain runs through an RPA.
-
- ✓ Do discuss site operations with an arboriculturist.
 - ✓ Do use toolbox talks to inform staff on site of the tree's needs.
 - ✓ Do liaise with the planning officer regularly to ensure full compliance at all times.
 - ✓ Do erect barriers such as RPA and CEZ fencing early.


RPA dos & don'ts




Don't use site vehicles within the root system, this will compact the soil and can lead to root suffocation.



Don't store poisons, chemicals, fuel, diesel, oil or cement beneath a tree. Don't light fires.

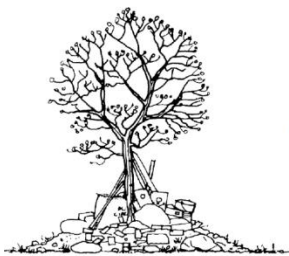

Don't store or deposit building materials against or beneath a tree.

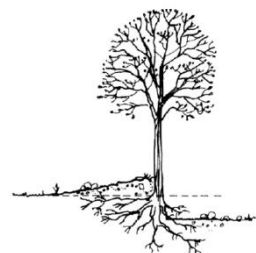

Excavations will damage roots, whilst increasing levels will exclude air vital for healthy roots.

Arboricultural Watching Brief (AWB)

When adequate tree protection and suitable distances to trees and rooting areas can be put in place on site, there is often no need for an Arboricultural Watching Brief (AWB). However, when the design dictates that work may be required in an area of sensitivity in regard to trees and rooting areas, an AWB may be required. You may also find that a planning authority places a planning condition on using an AWB on certain aspects of work.

It is strongly advised that you utilise the knowledge of your site arboriculturist/AWB. This advice should start to take place prior to any design ideas being formed. This can save many issues in regards to design and planning issues as you will know what will fit on site or not in relation to retained trees.

Common items where an AWB may be required:

- Installation of Tree Protection Fences.
- Movement of Tree Protection Fences.
- Work within or close to a tree RPA.
- Installation of piles within an RPA.
- Installation of temporary ground protection in or near tree rooting areas.
- Certain pruning needs for trees – specific and sensitive pruning.
- Excavation adjacent to rooting areas.
- Supervised hand or air spade work within a root protection area.
- Installation of ducting within a rooting area.
- Grading/blending of a bank batter to/from rooting area extremity.
- Overseeing soil nibbling to record the true extent of a rooting area radius.
- New planting locations. Locations and species selection.
- Crane operations past tree canopies.
- Removal of tree protection fences upon discharge of tree protection conditions for the site.
- Final landscaping and soil coverings from new back into existing soils/rooting areas.

The AWB is not there to hinder work but to advise on the best way forward to aid the project. This advice is based on known issues, experience and requirements of planning legislation.

Please feel free to ask JPTC any questions that you feel may require the use of and AWB. Most issues are easily resolved well before any damage to retained trees occurs if the advice is sought at an appropriate stage.

Tree Data

It is often essential to gain the tree information for the site first and then design the site around what the tree cover (following Arboricultural management work) allows.

A site's use can be maximised if the plans are drawn after the vegetation/tree survey is complete. This is to allow the architect to see exactly what area is available for development. A design which is correct and that fits the landscape, without causing significant disruption would then be achievable. This is particularly important if protected trees or trees of very high value are present. It is also far more likely to be accepted in the planning process.

Within the data captured on site, any immediate tree management work is also noted within the schedule of findings. This work is to help trees with minor problems and to increase site safety to construction workers and the new occupiers of the site following development.

The table on the following page is the cascade chart as per BS5837 2012 for capturing consistent tree data whilst carrying out development-based tree surveys. It allows for trees to be clearly seen by the planning process with a standardised, alpha numerical grading system. The alphabetical system also allows a colour coded approach to see the trees marked on a site plan according to its category (A, B, C & U). It is important to show tree canopy spreads in these standard colours, green, mid-blue, grey and red. Groups are shown as a pink area by JPTC.

Each tree/group is assessed to identify its species, capture its physical dimensions, assess its physiological health and assess its structural condition. Further assessment is made to how the tree is suited to the location where the proposed design is already known.

Trees which are in decline but have useful life left such as veteran trees are also included. This allows for them to be kept on sites where possible because of the high ecological, historic and cultural benefits they may bring to the locality. It is important to remember that these trees may be in excess of one hundred years old and their loss to the area could be dramatic for hydrology, ecology and landscape features not immediately obvious when stood on site.

The construction company's name is on the site, how the site is left, is how the site will be remembered. Trees may appear to be a nuisance to development processes but they should not be overlooked as they can add value to a site and reduce the future landscaping needs and associated costs.

Key to tree data classifications overleaf:

A separate large-scale version of this can be made available should it be required.

Table 1 Cascade chart for tree quality assessment

Category and definition	Criteria (including subcategories where appropriate)			Identification on plan
Trees unsuitable for retention (see Note)				
Category U Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years	- Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning) - Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline - Trees infected with pathogens of significance to the health and/or safety of other trees nearby, or very low quality trees suppressing adjacent trees of better quality <i>NOTE Category U trees can have existing or potential conservation value which it might be desirable to preserve; see 4.5.7.</i>			See Table 2
	1 Mainly arboricultural qualities	2 Mainly landscape qualities	3 Mainly cultural values, including conservation	
Trees to be considered for retention				
Category A Trees of high quality with an estimated remaining life expectancy of at least 40 years	Trees that are particularly good examples of their species, especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)	Trees, groups or woodlands of particular visual importance as arboricultural and/or landscape features	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)	See Table 2
Category B Trees of moderate quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of significant though remediable defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality necessary to merit the category A designation	Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little visual contribution to the wider locality	Trees with material conservation or other cultural value	See Table 2
Category C Trees of low quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150 mm	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories	Trees present in groups or woodlands, but without this conferring on them significantly greater collective landscape value; and/or trees offering low or only temporary/transient landscape benefits	Trees with no material conservation or other cultural value	See Table 2

Minimum Arboricultural Method Statement –

The list below must be in place before any development activity occurs on site, if in doubt ask, do not assume or carry on regardless.

1. **Before any construction plant equipment, vehicles and associated activities start** on site, carry out preliminary tree pruning/management works as listed within the tree schedules within this document subject to permissions from LPA – check for type, size and access for tree equipment to be used – get written approval from LPA for use. Permission will be required in writing from an LPA for trees subject to tree preservation orders and conservation areas - 211 notifications made if applicable if the area is a conservation area. Trees subject to a TPO also include the root system of the tree and soils in the vicinity of the tree.
2. No mechanical plant equipment is to access retained tree RPAs areas (marked as grey hatching) as noted on the site plan at the rear of this document at any stage – ground protection must be used and advice from an arboricultural watching brief advised if roots are under access routes. The same equipment/personnel must not use the construction exclusion zones. Storage of materials is also not allowed in the CEZ or tree RPAs or in a location where run-off can enter tree occupied soils.
3. Layout suitable rooting area and tree structure protection fences in accordance with BS5837 2012 or as type agreed by the LPA around retained tree's rooting areas, as defined in this document on the site plan. This temporary fence must remain until the LPA discharge the condition for the use of Tree Protection Fencing.
4. Mark RPA fences clearly to their intended use –

“Construction Exclusion Zone (CEZ) KEEP OUT”

These fences, once installed, must not be altered or moved without written permission.

5. No development work should take place within a theoretical rooting area of trees as defined by BS5837 2012 on site. Ample working room should be made available on site outside of RPA fences as a buffer zone.
No roots should be cut in excess of 10mm – seek immediate arboricultural advice if roots are found outside an RPA.
6. Protect all trees large and small plus future planting locations from development processes until the LPA discharge the tree protection condition.
7. Always use or seek the advice of the arboricultural watching brief if working adjacent to RPAs, lifting hard surfaces with possible roots below, working within 10m of a tree, woodland or tree group.
8. Ensure hedges have at least half their height available as a distance for an RPA.
9. Ensure any specific detailed AMS/toolbox talk details are written as required and signed off by LPA before undertaking any work.

Site Monitoring by AWB

In many cases the LPA will insist on site monitoring by the site arboriculturist at the site owner/project construction companies own cost, the results of which must be sent to the LPA within 72 hours of each visit.

By not carrying out conditioned site monitoring you will be in breach of your planning conditions and the condition cannot be discharged until you meet the condition on completion of all development work on site – impossible to do if frequent checks/records are not in place. The site monitoring needs to be tailored to the site. JPTC use the following list of headings with which to create the site monitoring sheet which can be sent to the LPA.

Site Address:

POC:

Date:

Trees on or off site:

Timings/visit chronology:

1. Pre start visit.
2. Tree Protection Fencing in place – AWB check, photos to LPA to be agreed and signed off.
3. Site occupation by contractor.
4. Monthly checks.
5. Completion of all works with a risk to trees.
6. Tree Protection Fencing removal/Tree Protection Fencing condition discharge.

Checks

- Tree protection (RPA) fences in place:
- RPA Fence signage fitted:
- Evidence of movement or tampering:
- RPA Fences at correct distances to tree stems:
- Service installations not affecting trees:
- Groundwork completed:
- Tree work completed:
- Materials stored away from RPA's and CEZs:
- Specific planning condition requirements met:

Summary

A summary of the findings on site.

Photos from site

Photographs to use as pictorial evidence that the above records are true and correct.

Arboricultural Implications Assessment – AIA (surveyor's overall thoughts)

This AIA has been written by the tree surveyor for the site and is based upon tree condition, relationship to the site and potential future use or simply to explain obvious arboricultural constraints, tree threats or management issues – discussion that is useful for the Tree Officer looking at the application and also the architect/site manager. Page 7 in this document should be read and understood. It is strongly recommended that arb input occurs in the layout process to avoid planning issues regarding trees at a later stage.

Site monitoring will be required as per page 21 of this document. This should include and pre start meeting, Tree Protection Fence install, mid-point and end point visits with the findings of each visit sent to the LPA.

I have seen the proposed layout for the Lodge area. It would appear to have been designed based on general area dimensions and not following suitable tree advice as laid in BS5837 2012. The design has a significant footprint that covers the majority of trees on site meaning clashes are inevitable with high value and low value trees. Following my visit to the park, it is clear that there are a number of trees in the project locality that pose a public risk currently. These trees will require felling/making safe due to the area of the park affected being high use. This should take place remote of the project. These are trees 2, 3, tag 4114, trees 9 and 10, there are also other trees likely to be elevated to this list from adjacent trees and groups.

G1 and G2 contain a high number of defect trees. These range from poor form, non-tensile main structural unions, decline or poor location. Retention is not desirable of either group. New planting will be far better for the site long term both for local landscape and site safety.

Trees 1, 6, 7 and 8 are trees that are low value and are most likely going to be removed. It would make no sense to design around these trees for them to then decline further and become a hazard. This would need to be an internal NCC management discussion with the design team, tree officers and site arboriculturist.

Trees 4 & 5 along with groups 3, 4 & 5 are all high retention category trees. They do not have obvious major defects but may require minor arboricultural management in accordance with good management practices. These trees will all require tree protection fences (unless T4 is also removed) – these protection fences must be assessed and checked for appropriateness by the site arboriculturist before any demolition or construction equipment enters the site.

Site space is limited. The area has significant public and vehicle access. Signing and guarding the site will be difficult. Careful planning and execution of site safety will be required. Limited site space also places greater pressure on trees.

New planting will be required and in significant numbers in order to replace trees that will need to be removed – care and consideration of species chosen must take place. Some species need not be replaced such as Leyland cypress and larger species such as cedars. Appropriate soil volumes must be provided for all new plantings. Planting must take place at the best time of year for planting – early in the planting season, October to late December at the latest. It is strongly advised not to plant after Christmas.

Tree Work List

Felling list

T1? T2, T3. T7? T8? T9 and T10. G1 and G2. Tag 4114 from G3.

Pruning works

T6. G4 and G5.

Coppicing works

None.

Transplanting works

None.

Planting list

Approximately 25 strong landscape trees will be required for replacement planting. It is essential planting is carried out between October and late December – do not plant after Christmas.

Data Sheets - site survey carried out - 26/07/2023

The following data tables contain specific tree dimensions that are used to calculate the relevant protection from development. This protection is to ensure the long-term survival of retained trees. Should any questions arise please contact Treecare Consulting.

Individual Trees Schedule:

Tree Number	Species	Height	Tag Number	Spread N - E - S - W	Low Limb Height	Low Limb Direction	Stems	Diameter @ 1.5m in MM	Structural Condition	Physiological Condition	Noted defects	Management Recommendations	Age Class	Years Remaining	Tree Quality	Tree Value	AMS Comment
T1	Cherry	8	4112	5 5 5 5	3	All round	1	340	Damaged	Fair	Girdling roots. Decay in pruning wounds. Proximity to building.	Reduce crown by up to 2m ASLB using NTP or consider tree replacement	Mature	10+	C Low Quality	2 Landscape value	Potential replacement tree
T2	Malus	5	4113	4 4 4 4	3	All round	1	260	Damaged	Fair	Inonotus hispidus fungal brackets on main structural limbs/fork	Fell and replace tree	Mature	Dangerous 0	U Un-gradable in 5837	U Un-gradable in 5837	Replacement tree required
T3	Cedar	18	4115	6 2 3 6	3	All round	1	400	Damaged	Dead	Standing dead tree	Fell	Mature	Dangerous 0	U Un-gradable in 5837	U Un-gradable in 5837	Replacement tree required
T4	Birch	18	4116	7 5 5 6	5	All round	1	500	Normal for species	Normal for species	No major defects noted	None	Mature	20+	A High Quality	1 Arb Values	CEZ around tree and rooting area
T5	Oak	18	4117	6 6 6 6	3	All round	1	470	Normal for species	Normal for species	Dead wood, low foliage	Remove all dead wood from crown. Lift foliage to 6m over access	Mature	40+	A High Quality	2 Landscape value	CEZ around tree and rooting area
T6	Birch	16	4118	5 4 2 5	4	N	1	330	Damaged	Normal for species	Hung up branches in crown. Low limb over access.	Remove damaged branches. Remove low limb over access and epicormic shoots using NTP	Mature	10+	C Low Quality	2 Landscape value	CEZ around tree and rooting area
T7	Ash	20	752	8 8 8 8	4	All round	1	600	Damaged	Fair	HF1 infection. Significant dead wood	Remove dead wood minimum. Consider fell and replace	Mature	less than 10	C Low Quality	2 Landscape value	Potential replacement tree

Tredegar Park Lodge

Tree Number	Species	Height	Tag Number	Spread N - E - S - W	Low Limb Height	Low Limb Direction	Stems	Diameter @ 1.5m in MM	Structural Condition	Physiological Condition	Noted defects	Management Recommendations	Age Class	Years Remaining	Tree Quality	Tree Value	AMS Comment
T8	Ash	18	4119	7 7 7 7	5	All round	1	500	Damaged	Poor	HF2+ infection. Significant dead wood. Conflict with adjacent ground structures	Remove dead wood minimum. Consider fell and replace	Mature	less than 10	C Low Quality	2 Landscape value	Potential replacement tree
T9	Cherry	9	4120	4 4 4 4	2	All round	1	450	Hazardous defect/tree	Fair	Main union non tensile with decay present. Proximity to highway	Fell and replace tree	Mature	Dangerous 0	U Un-gradable in 5837	U Un-gradable in 5837	Replacement tree required
T10	Cherry	16	4121	4 4 4 4	3	All round	1	450	Hazardous defect/tree	Fair	Stem decay - ants nest within. Split scaffold limb fork. Proximity to access. Altered exposure	Fell and replace tree	Mature	Dangerous 0	U Un-gradable in 5837	U Un-gradable in 5837	Replacement tree required

Tredegear Park Lodge

Groups of Trees Schedule:

Group Number	Species	Low Limb Height	Low Limb Direction	Average group height	Expected RPA (stem to fence M)	Prelim RPA fence locations	Structural Condition	Physiological Condition	Noted defects	Management Recommendations	Age Class	Years Remaining	Tree Quality	Tree Value	AMS Comment
G1	Birch	Ground level	All round	16	5	Follow feature edge	Normal for species	Normal for species	Trees clashing with adjacent structures. Hostile rooting areas.	Fell	Mature	less than 10	C Low Quality	2 Landscape value	Fell due to conflict with location
G2	Mixed	3	All round	16	5	Follow feature edge	Characteristic defect	Characteristic defects present	Dying ash, clashes with structures, poor form, decay in 17 mixed species trees.	Clear all trees from internal garden area but allow for significant high value replacement planting	Mature	less than 10	C Low Quality	2 Landscape value	Fell due to conflict with location. Significant replacement re planting required
G3	Mixed	3	All round	17	5	Follow feature edge	Normal for species	Normal for species	Dead Birch tag 4114. Dead wood in remaining tree crowns.	Fell tag 4114 and remove dead wood over access road.	Mature	20+	B Moderate Quality	2 Landscape value	Carryout tree work and create CEZ
G4	Mixed	3	All round	16	5	Follow feature edge	Characteristic defect	Normal for species	Dead wood and low foliage over access road	Lift foliage tips over access road to 6m. Remove dead wood.	Mature	20+	B Moderate Quality	1 Arb Values	Carryout tree work and create CEZ
G5	Mixed	2	All round	16	5	Follow feature edge	Characteristic defect	Normal for species	Low foliage over access route	Lift foliage to 6m over access route to 6m	Mature	20+	B Moderate Quality	2 Landscape value	Carryout tree work and create CEZ

Site Plans – Key

Scale plans can be sent as PDF files if required. The plans are to indicate locations of trees, locations of main objects on site and the location of tree protection fencing. Stem diameters found in tree and tree group data tables should be used to mark out the location of root protection fencing on site.

Dark Red U = trees requiring removal due to condition/grade.

Grey = C Class trees (low value).

Blue = B Class trees (moderate value).

Green = A Class trees (high value).

Grey hatched area = Root protection areas (RPA).

Black dash line = Tree protective fence locations.

Shade quadrants = Hatched grey fan area.

ALL SITE PLANS CAN BE PRINTED AS A3 OR BE SENT AS DXF FILES. ALTERNATIVELY THE CSV FILE CAN BE EMAILED WITH TREE DATA ON.

Tredegar Park Lodge

Site Plan (Screen grab – please see scale pdf plan)

