



1:500 @ A1

TREE REMOVAL/PROTECTION KEY:


- DEVELOPMENT BOUNDARY
- OWNERSHIP BOUNDARY
- EXISTING TREES & TREE GROUPS
To be retained.
- ROOT PROTECTION AREA
To be retained as per BS5837 standard.
- TREE PROTECTION FENCING
Heras fencing to be installed as per BS5837:2012 figure 1 below
- EXISTING TREES & TREE GROUPS
To be removed with tree ID numbers.
- PROPOSED TREES
Refer to SMS-HLM-XX-00-D-L-4501 Soft Landscape Plan for details

This drawing is to be read in conjunction with the following Arboricultural documents produced by Steve Ambler & Sons Tree Specialists Ltd:

Tree Constraints Plan (August 2023)

BRITISH STANDARD 5837:2012

Figure 1: Example of above-ground stabilizing system

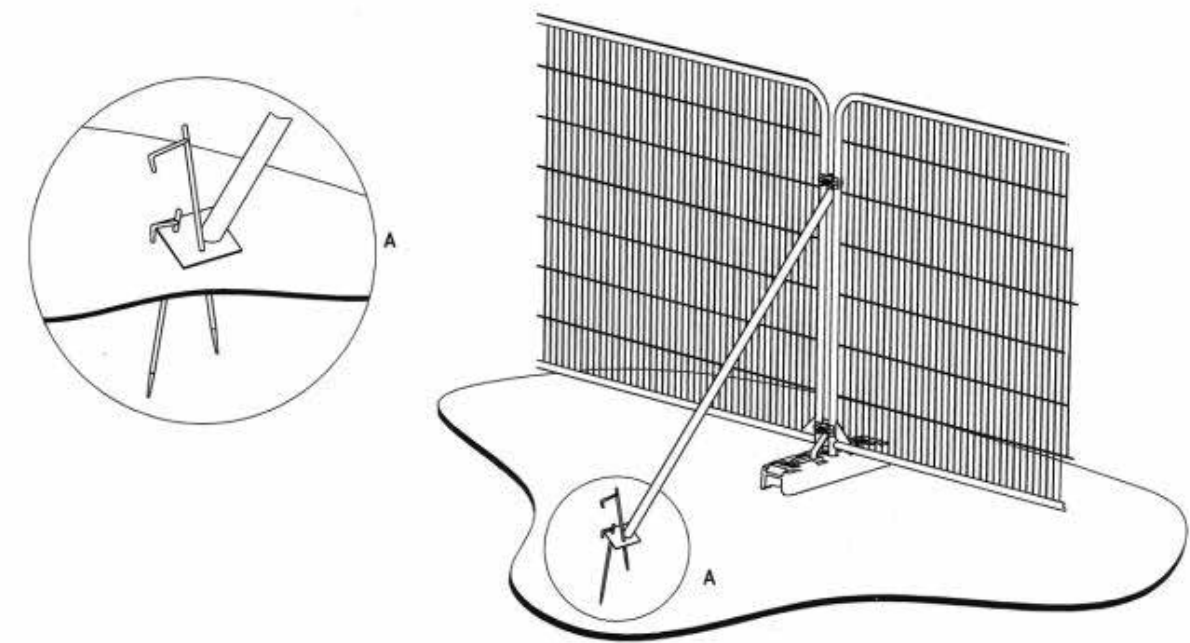

a) Stabilizer strut with base plate secured with ground pins

GENERAL NOTES
No tree felling to be carried out during the bird nesting season, from February to August.

- All tree protection fencing to be fully installed prior to any of the following taking place:
- Plant and material delivery
 - Demolition
 - Soil stripping
 - Construction Works
 - Utility Installation
 - Landscaping

All weather notices should be attached to the barrier with the words such as:
'CONSTRUCTION EXCLUSION ZONE - NO ACCESS'

Once erected all tree protection fencing will be regarded as sacrosanct and will not be removed or altered without prior recommendation by the landscape architect, arboriculturalist and local planning authority.

Inside the exclusion area of the tree protection fencing the following shall apply:

- No mechanical excavation whatsoever
- No excavation by any other means without arboricultural site supervision
- No hand digging without a written method statement having first been approved by the arboriculturalist
- No lowering of levels for any purpose
- No storage of plant or material
- No storage or handling of any chemicals including cement washings
- No vehicular access
- No fires in addition to the above, further precautions are necessary adjacent to trees:
 - A 10m separation zone shall be observed between any tree and substances injurious to health, including fuels, oil, bitumen, cement (including cement washings), builders sand, concrete mixing and other chemicals.
 - No fire shall be lit such that flames come within a 5m of tree foliage.

Notes

Check all dimensions on site. Do not scale from this drawing
Report any discrepancies and omissions to HLM Architects
This Drawing is Copyright ©

DRAWING NOTES:

- This drawing must be read in conjunction with other HLM Architects' construction drawings, landscape specification, and relevant documentation from other disciplines.
- The contractor is responsible for verifying all dimensions, levels, and coordinates on-site prior to commencement. Any discrepancies must be reported immediately.
- Any discrepancies between drawings and site conditions must be reported to HLM Architects before proceeding.
- All works must comply with the latest British Standards, Building Regulations, and relevant codes of practice.
- The contractor is responsible for coordinating with all disciplines to ensure full integration of the design.
- The contractor must comply with CDM Regulations and all statutory health and safety requirements.
- Only the latest revision of this drawing should be used. The contractor must ensure they are working from the most current information.
- Works must adhere to the approved fire strategy and accessibility requirements in accordance with Building Regulations
- Any changes or proposed substitutions to specified materials must be reviewed and approved by the design team.
- Any proposed material substitutions must be 10. approved in writing before implementation.
- The contractor is responsible for all temporary works and ensuring site safety during construction.

P010	PLANNING AMENDMENT	15/08/25	AC	KM
P09	FOR TENDER	22/07/25	AC	KM
P08	CONSTRUCTION ISSUE			
P07	STAGE 4 UPDATE	15/08/24	VT	MS
P06	STAGE 4 UPDATE	07/08/24	VT	MS
P05	STAGE 4 ISSUE	19/07/24	VT	MS
P04	DRAFT STAGE 4 ISSUE	27/06/23	VT	MS
P03	ISSUE FOR PLANNING	29/01/24	VT	MS
P02	ISSUE FOR PLANNING	23/01/24	AC	MS
P01	STAGE 3 ISSUE	04/08/23	VT	MS
Rev	Description	Date	By	Chk

Revisions	Suitability
Project	C1

St Mary's RC School Landscape

Client


NEWPORT CITY COUNCIL/NEWPORT NORSE

Title

TREE REMOVAL AND PROTECTION PLAN

Drawing No.	Revision
SMS-HLM-XX-00-D-L-4502	P010

Scale	Drawn
As indicated @A1	AC
Date	Checked
15/08/25	KM



© HLMArchitects
2nd Floor
Ailsa Court
121 West Regent Street
Glasgow G2 2SD

www.hlmarchitects.com
T. +44 (0) 141 226 8320
F. +44 (0) 141 226 8350
glasgow@hlmarchitects.com

1:500 1:300 50 M 20 M
