

Job Name	Drake House, Langstone, Newport	Job Number	1228	Date	14.02.25
----------	--	------------	-------------	------	-----------------

Site Report – Final snagging


The above site was inspected on the 14th February 2025 at 12.00pm by Dan Patterson of dp landscape architecture [DPLA]. This report assesses the completed work against DPLA drawing number 1228.01.

General comments:

The new hedge has been completed in accordance with the above drawing. The species used [hornbeam] appears to be correct.

The height of the new planting is acceptable and the spacing / planting density is correct. Plant numbers are also in line with the drawing and bark mulch is in place to the correct depth.

The plants themselves appear to be good quality and have been planted correctly.

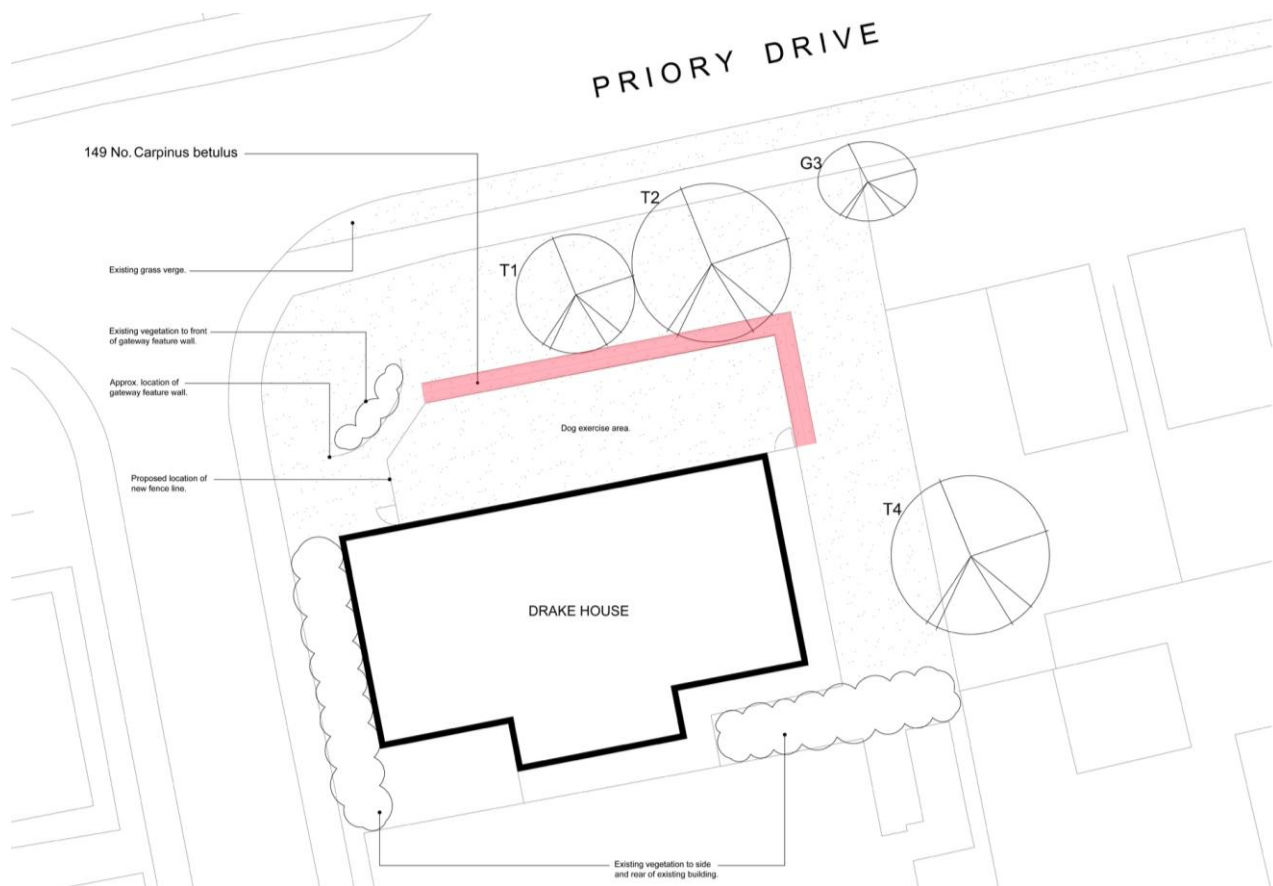

Recommendations:

There is a very narrow strip of grass between the hedge and the fence line. See photographs below. It would be beneficial to remove / kill off this grass to avoid any future maintenance issues. The gap should be filled with bark, up to the fence line.



Before and after photos:



Before.



After.

Next steps:

The next site visit [year 2] is planned for next summer with a report to be issued before 31st July 2026.
